HIGH LEVEL PROGRAM - UNSW J12 & K15 ANFF Labs (REV5. 18-09-19)
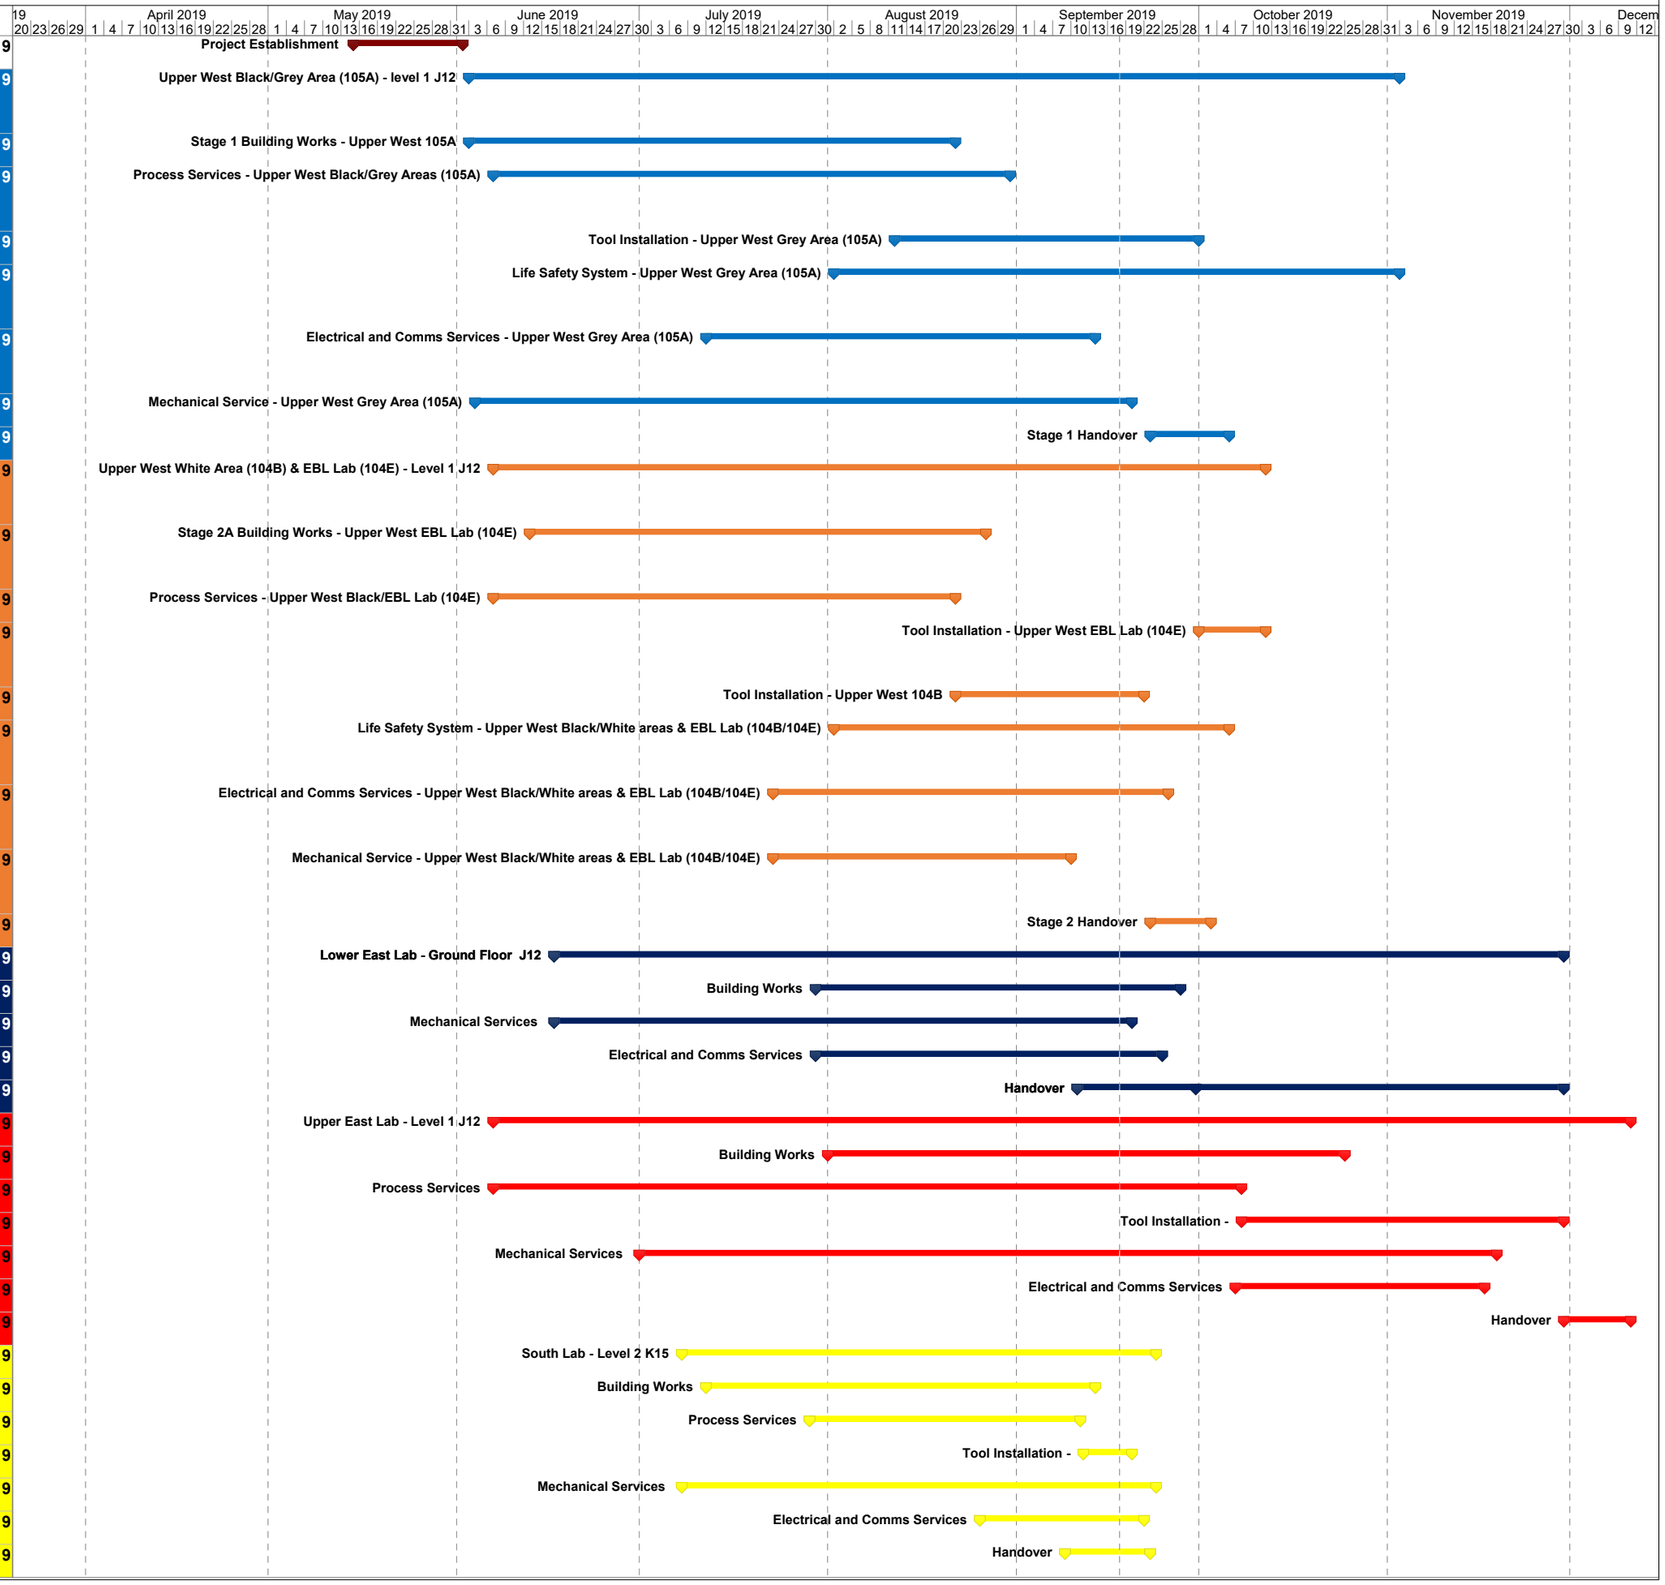
ID	Task Name	Duration	Start	Finish
1	**Project Establishment**	**16 days**	**Wed 15/05/19**	**Sat 1/06/19**
6	**Upper West Black/Grey Area (105A) - level 1 J12**	**131 days**	**Mon 3/06/19**	**Sat 2/11/19**
7	**Stage 1 Building Works - Upper West 105A**	**68 days**	**Mon 3/06/19**	**Wed 21/08/19**
15	**Process Services - Upper West Black/Grey Areas (105A)**	**72 days**	**Fri 7/06/19**	**Fri 30/08/19**
26	**Tool Installation - Upper West Grey Area (105A)**	**43 days**	**Mon 12/08/19**	**Mon 30/09/19**
43	**Life Safety System - Upper West Grey Area (105A)**	**80 days**	**Fri 2/08/19**	**Sat 2/11/19**
52	**Electrical and Comms Services - Upper West Grey Area (105A)**	**55 days**	**Fri 12/07/19**	**Fri 13/09/19**
60	**Mechanical Service - Upper West Grey Area (105**	**92 days**	**Tue 4/06/19**	**Thu 19/09/19**
68	**Stage 1 Handover**	**12 days**	**Mon 23/09/19**	**Sat 5/10/19**
73	**Upper West White Area (104B) & EBL Lab (104E) - Level 1 J12**	**108 days**	**Fri 7/06/19**	**Fri 11/10/19**
74	**Stage 2A Building Works - Upper West EBL Lab (104E)**	**64 days**	**Thu 13/06/19**	**Mon 26/08/19**
81	**Process Services - Upper West Black/EBL Lab (1**	**64 days**	**Fri 7/06/19**	**Wed 21/08/19**
91	**Tool Installation - Upper West EBL Lab (104E)**	**10 days**	**Tue 1/10/19**	**Fri 11/10/19**
96	**Tool Installation - Upper West 104B**	**27 days**	**Thu 22/08/19**	**Sat 21/09/19**
108	**Life Safety System - Upper West Black/White areas & EBL Lab (104B/104E)**	**56 days**	**Fri 2/08/19**	**Sat 5/10/19**
116	**Electrical and Comms Services - Upper West Black/White areas & EBL Lab (104B/104E)**	**56 days**	**Tue 23/07/19**	**Wed 25/09/19**
123	**Mechanical Service - Upper West Black/White areas & EBL Lab (104B/104E)**	**42 days**	**Tue 23/07/19**	**Mon 9/09/19**
132	**Stage 2 Handover**	**9 days**	**Mon 23/09/19**	**Wed 2/10/19**
137	**Lower East Lab - Ground Floor J12**	**143 days**	**Mon 17/06/19**	**Fri 29/11/19**
138	**Building Works**	**52 days**	**Tue 30/07/19**	**Fri 27/09/19**
149	**Mechanical Services**	**82 days**	**Mon 17/06/19**	**Thu 19/09/19**
158	**Electrical and Comms Services**	**49 days**	**Tue 30/07/19**	**Tue 24/09/19**
166	**Handover**	**69 days**	**Wed 11/09/19**	**Fri 29/11/19**
171	**Upper East Lab - Level 1 J12**	**159 days?**	**Fri 7/06/19**	**Tue 10/12/19**
172	**Building Works**	**73 days?**	**Thu 1/08/19**	**Thu 24/10/19**
182	**Process Services**	**104 days**	**Fri 7/06/19**	**Mon 7/10/19**
191	**Tool Installation -**	**46 days**	**Tue 8/10/19**	**Fri 29/11/19**
206	**Mechanical Services**	**121 days**	**Mon 1/07/19**	**Mon 18/11/19**
214	**Electrical and Comms Services**	**36 days**	**Mon 7/10/19**	**Sat 16/11/19**
221	**Handover**	**9 days**	**Sat 30/11/19**	**Tue 10/12/19**
226	**South Lab - Level 2 K15**	**67 days**	**Mon 8/07/19**	**Mon 23/09/19**
227	**Building Works**	**55 days**	**Fri 12/07/19**	**Fri 13/09/19**
234	**Process Services**	**38.5 days**	**Mon 29/07/19**	**Wed 11/09/19**
237	**Tool Installation -**	**7 days**	**Thu 12/09/19**	**Thu 19/09/19**
252	**Mechanical Services**	**67 days**	**Mon 8/07/19**	**Mon 23/09/19**
260	**Electrical and Comms Services**	**24 days**	**Mon 26/08/19**	**Sat 21/09/19**
267	**Handover**	**12 days**	**Mon 9/09/19**	**Mon 23/09/19**
